

HAMMER MAKING PROJECT

HMP

STEINWAY & SONS

CHECKLIST – PROJECT CRITERIA

Please fill out the following forms. Fields marked with * are compulsory for project approval. Fields marked with ° need to be filled with proposals and will be reviewed by the management.

Project criteria

THE PROJECT…	CHECK?*	COMMENT *(optional)*
…is non-repetitive and the scope exceeds day-to-day work.	yes	…
…takes more than 1 month.	I am afraid it does	
…requires multiple permanent project members from different departments.	yes	
…-sponsor is from the top-management.	yes	

TARGET DEFINITION AND BENEFITS DESCRIPTION

Master Data

PROJECT NAME*	Hammer making project	SPONSOR°	Olaf Gube
STEERING COMMITTEE°	Christian Mayer, Rudi Wyrsch, Sun Jin Kim, Olaf Gube, Rob Polan?		
PROJECT MANAGER°	Clemens Kunert	CO-PROJECT MANAGER°	Lachmann
START-DATE°	September 2022	PROJECT SIZE°	Large
END-DATE°	August 2023	PROJECT TYPE°	Development

TARGET DEFINITION AND BENEFITS DESCRIPTION

Master Data

Question and answer form (part 1)

PROBLEM / CURRENT CONDITION*	1. Renner hammers are good but not outstanding. Competition products are close or even better. 2. Knowledge of hammer making/ development is neither perfect nor complete 3. Many different ideas are in discussion and testing and needed to be consolidated and structured
TARGET DESCRIPTION / PROJECT GOAL*	1. We make hammers for Steinway and Boston which require minimal treatment after installation (even more important for the OEMs). 2. The hammers will be very similar set by set so that the same voicing method can be used set by set to achieve a similar tonal outcome 3. We make hammers for Steinway and Boston which are improving the tonal quality of the pianos 4. We understand the leading factors of good hammer making and how these are influential to each other
TASKS*	1. All information existing needs to be gathered and analyzed. Conclusions need to be drawn from it. 2. We need to understand and describe what a good hammer is for Steinway and Boston 3. Tests need to be set up to understand the importance of the different parameters – it is crucial to find a test set up that allows a quick feedback about the result 4. We know how to compose a good hammer and ensure to sustain the knowledge we gain

TARGET DEFINITION AND BENEFITS DESCRIPTION

Question and answer form (part 2)

INDICATORS FOR ACHIEVEMENT*	1. Recipes for Steinway HH, NY and Boston hammers are approved by the constituencies 2. Hammers are close to the bounce curve of voiced reference hammers when leaving the press
PERMANENT PROJECT TEAM°	• Clemens Kunert • Kalle Lachmann • Herr Wilke • Justin (vielleicht als Experte und nicht als permantentes Projektmitglied) • Voicer/ piano technician- mit Frau Kim besprechen
REPORTING°	Monthly to steering committee and to customers if applicable
PRE-CONDITIONS*	The new hammer press needs to be available for testing. No hammer presses will be used for testing which are not NC controlled.

Fields marked with * are compulsory for project approval. Fields marked with ° need to be filled with proposals and will be reviewed by the management.


TARGET DEFINITION AND BENEFITS DESCRIPTION

Question and answer form (part 2)

POSSIBLE RISKS*	• Renner looses customers since we are not competitive • Steinway product quality cannot be optimized • We might not be able to deliver hammers for Boston or NY • We are not able to understand the hammer making process well • We don‘t find an end • We make Steinways competition stronger • Knowledge we gain might not fit to the mass production
NON-GOALS*	n.a.
DEPENDENT / RELATED PROJECTS*	• 10YGP – HH – voicing capacity should be positively develop when hammers are easier to voice • QIP – NY, can be a big step forward

SCHEMATIC PROJECT PROCESS*°

Please adapt the following chart to display the rough project process. No exact GANTT needed. Feel free to add annotations.

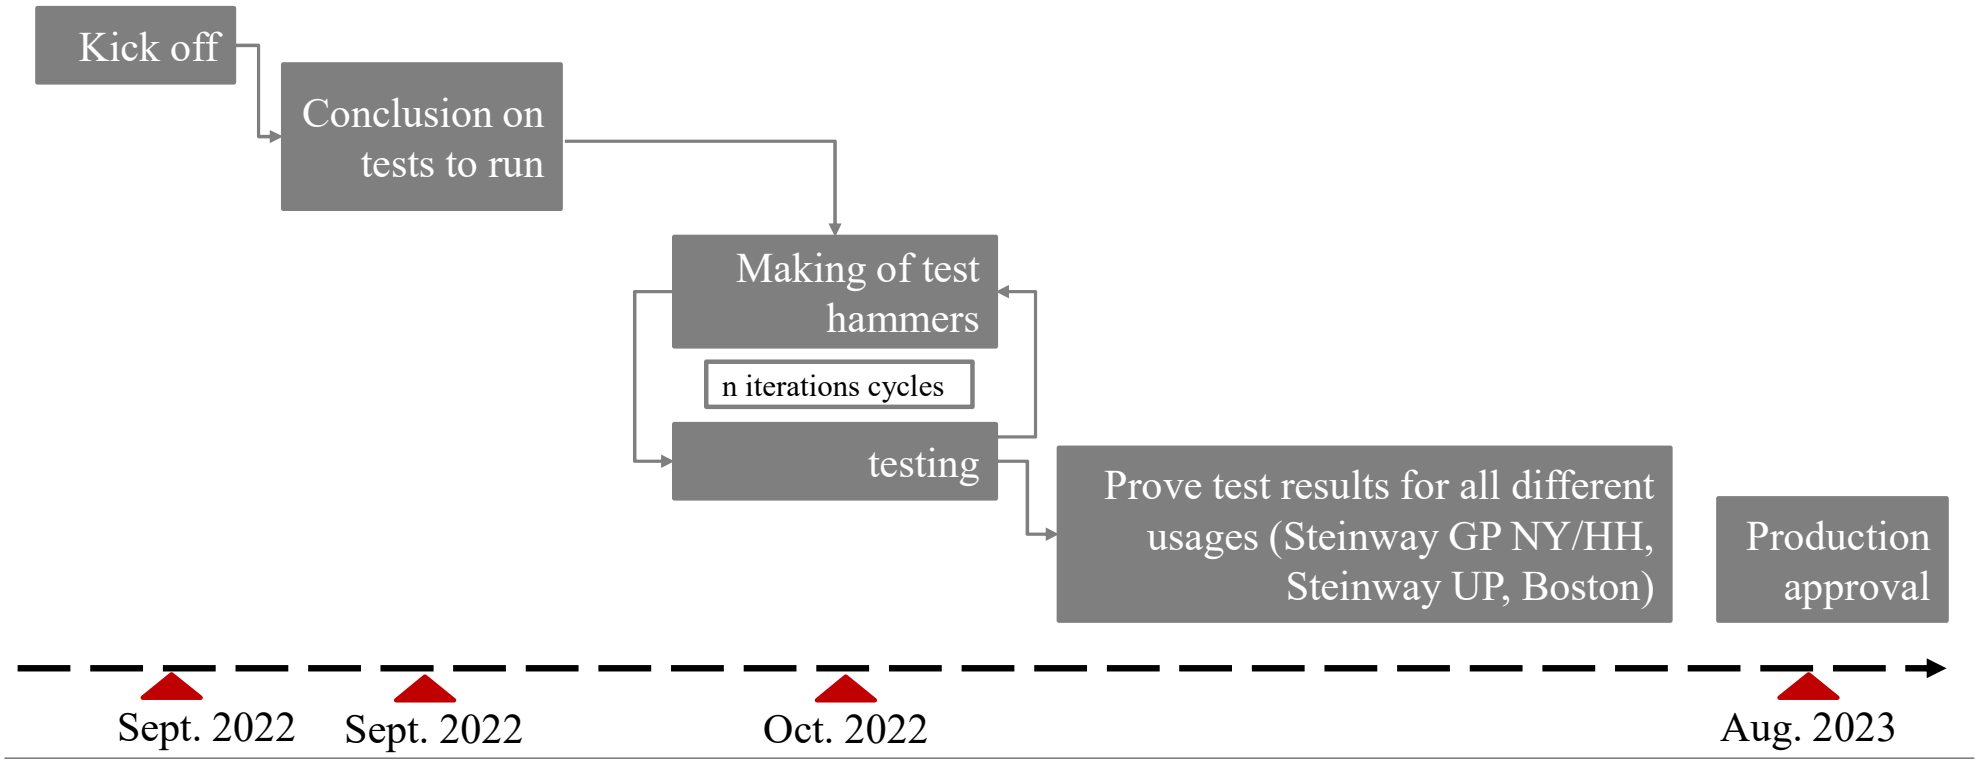

Fields marked with * are compulsory for project approval. Fields marked with ° need to be filled with proposals and will be reviewed by the management.

STEINWAY & SONS

APPENDIX

Feel free to insert any data that could serve to describe the project scope in more detail.

PROJECT HISTORY

Project Idea

INITIATOR	Name	DATE DOC. HANDED IN	Date (DD/MM/YYYY)

Project Approved

SPONSOR	Name	DATE PROJECT APPROVED	Date (DD/MM/YYYY)

Project Execution

PROJECT MANAGER	Name	DATE PROJECT START	Date (DD/MM/YYYY)
RELEVANT CHANGE?	Description of change	RELEVANT CHANGE?	Description of change
RELEVANT CHANGE?	Description of change	RELEVANT CHANGE?	Description of change
RELEVANT CHANGE?	Description of change	RELEVANT CHANGE?	Description of change

Project Closure

PROJECT GRADE	1 (very good) – 6 (very bad)	DATE PROJECT CLOSURE	Date (DD/MM/YYYY)
